


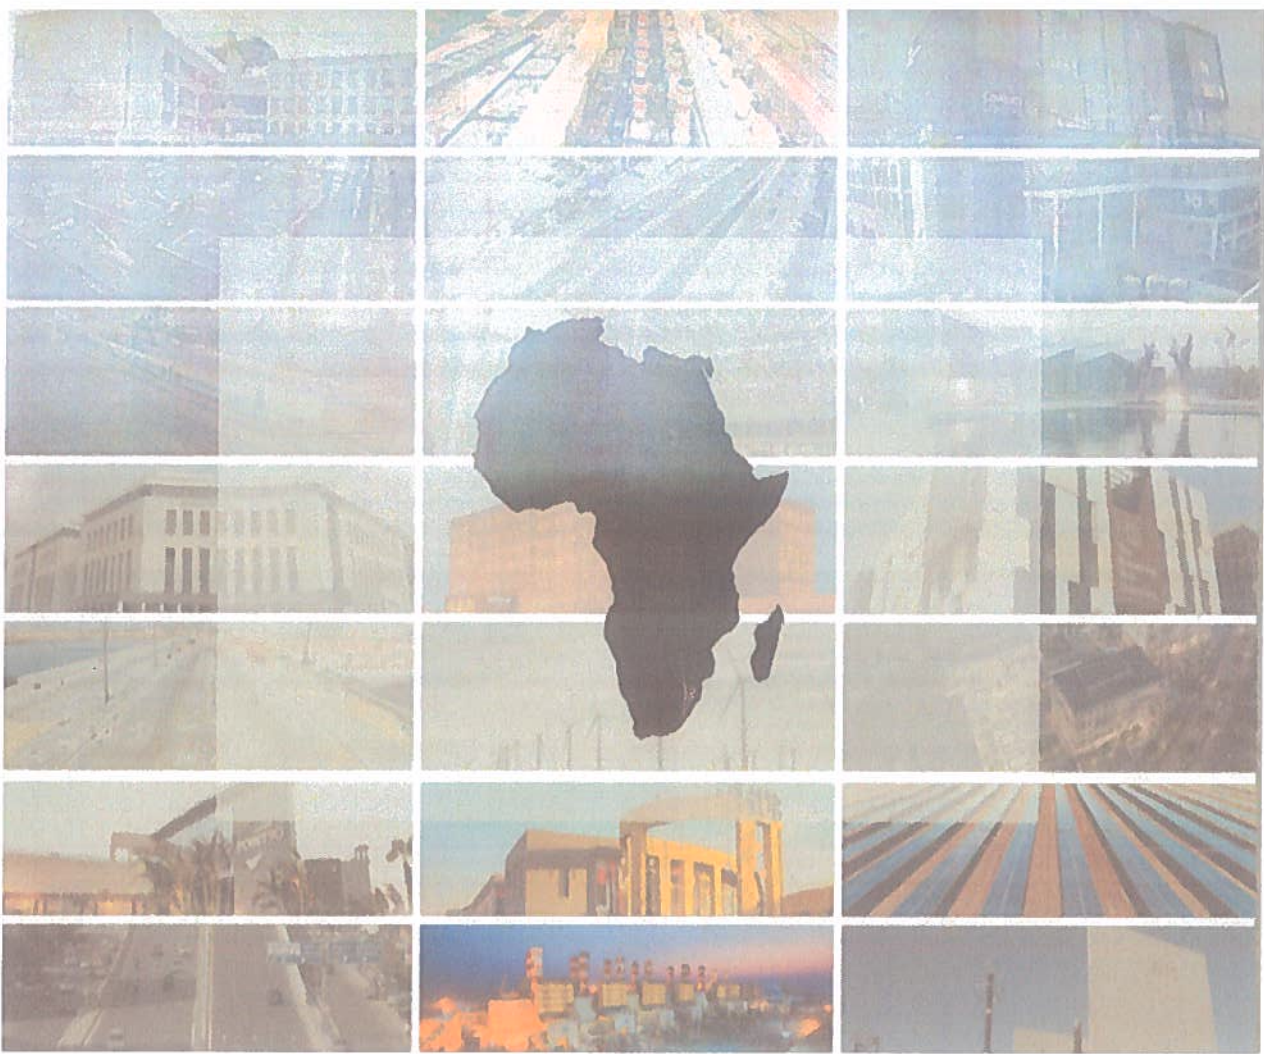

ROWAD
MODERN ENGINEERING

El Sadat Factory Production Process

P-OP-11

Prepared by:

Mohamed Abdel Razek

Production Manager

Sameh Herazy

QC Department Manager

Adham Edward

Purchasing Manager

Ahmed Helmy

Procurement Manager

Youssef Kamal

Formwork & Self Execution Manager

Reviewed by:

Mohamed Ragab

COO

Tarek Ayoub

VP

Approved by:

Mohamed Mahlab

CEO

May, 2025

1. OBJECTIVES

The objective of this process is to ensure the continuous and efficient operation of the factory by delivering products to Rowad projects that fully comply with the required specifications, adhere to the defined budget, and meet established quality standards.

2. STAKEHOLDER

- Project Manager
- Production Manager
- QC Engineer (Project)
- Storekeeper

3. LIABLE STAKEHOLDER

- Project Requester
- Project Manager
- QC (Project)
- Production Manager
- HO Procurement
- HO Purchasing
- Storekeeper
- VP
- Supplier

4. TERMS AND DEFINITION

- **H.O:** Head Office
- **QC:** Quality Control
- **PR:** Purchase Request
- **PO:** Purchase Order
- **SD:** Shop Drawing
- **CS:** Comparison Sheet
- **IMIR:** Internal Inspection Request
- **MRV:** Material Received Voucher

5. RELATED DOCUMENTED INFORMATION

- Internal PR “ERP”
- PO “ERP”
- IMIR
- Production Factory Plan, F-P-OP-11-01
- Preventive Maintenance Plan, F-P-OP-11-02
- Quarterly Factory Report, F-P-OP-11-03
- Release for Fabrication, F-P-OP-11-04
- Request for Return/Transfer Material, F-P-FN-01-01
- Supply-Apply Comparison Sheet, F-P-VMO-01-08
- Measuring Equipment Calibration Log, F-P-QD-03-01

6. PROCESS DETAILS

6.1 PROCES INPUT

- Projects Specs & Needs
- Project RFQ
- ITP

6.2 PROCESS OPERATIONS

Sr	Process Cycle Description	Responsibility	Forms
Project Requests			
1	Project requester shall send the RFQ with the requested QTYs, attached specs, design/shop drawings, supplying schedule as per the project needs to Sadat Factory Production Manager.	Project Requester	RFQ
2	Production Manager shall prepare a quotation based on the QS, approved SD, approved specs & painting system provided by Site T.O Manager for the requested project and send it to H.O Procurement.	Production Manager Site TO Manager	Production Factory Plan F-P-OP-11-01
3	H.O Procurement shall prepare CS between El-Sadat factory and other S/Cs.	H.O Procurement	Supply-Apply Comparison Sheet F-P-VMO-01-08
4	In case El-Sadat factory is selected, H.O Procurement shall send the approved CS to the Project Requester.	H.O Procurement	
5	Project Requester shall create an internal PR with the requested QTYs via Oracle, attached approved CS.	Project Requester Production Manager	Internal PR (ERP)

Sr	Process Cycle Description	Responsibility	Forms
	Internal PR shall be approved by Production Manager, Direct (FW & SE) Manager & VP.	Direct Manager VP	
6	In case material is available at El-Sadat factory or transferred from any project to the factory via Oracle by storekeeper, Production Manager shall issue Release for Fabrication to be approved by QC after material inspection/ testing. Project Manager is responsible for immediately allocating the required expenses to conduct all the necessary tests. Release for Fabrication to be attached to Job Order when issued. If material is not available, external PR for the raw materials shall be created by the Production Manager via Oracle along with the delivery schedule. CS to be prepared by Purchasing based on the evaluated vendor list and approved ones by QC team. Purchasing shall notify project's QC via e-mail for material sampling and testing prior to PO issuance. QC shall provide feedback to the Purchasing via e-mail within 48 hours. Purchasing dep. shall proceed in issuing the PO. (Refer to Purchasing Process P-PU-01)	Production Manager QC	Release for Fabrication F-P-OP-11-04 Request for Return/Transfer Material F-P-FN-01-01
7	Job order to be issued via Oracle with the Parent code (including the raw material and indirect cost) to be allocated on the requested project. Accordingly, the Production Manager shall update the production factory plan.		Production Factory Plan F-P-OP-11-01
Supply, Inspection & Storage			
8	Factory Production Manager shall notify the concerned Project Manager & QC Manager immediately with the delivered material to conduct the technical inspection with necessary tests to carry out & receive the test results within 14 days to comply the supplier contractual terms. Production Manager shall issue Release for Fabrication to be approved by QC after material inspection/ testing.	Storekeeper Project QC Engineer	IMIR (ERP)
9	In case material is rejected, storekeeper shall segregate the rejected materials, set aside with the label "Rejected" and notification to be sent to the Purchasing department, Project Manager & Factory Production Manager by QC Manager.	Storekeeper	

Sr	Process Cycle Description	Responsibility	Forms
10	Material shall be stored according to the technical specifications' conditions. (Refer to Material Control Process P-FN-01)	Storekeeper	
Manufacturing & Handling			
11	Production Manager shall start the manufacturing phase as per the SD, Project specs and agreed production plan. Mock up sample shall be prepared & delivered to site to acquire the client's approval prior to mass production. Project QC/Third Party (If required) shall inspect the product during the production phase at Sadat workshop/outsourced subcontractors, according to the approved fabrication ITP. Technical Office Manager shall provide the outsourced subcontractors with all SDs, Project specs & agreed production plan or any related fabrication documents along with the contract to be signed.	Production Manager Project QC	
12	Production Manager shall notify the project's Project Manager to handle the logistics cycle to receive the fabricated items after receiving the shipping release form from the responsible QC.	Production Manager Project Manager	
13	Project Storekeeper shall notify project's QC Manger to inspect the final product upon delivery on the project site. Refer to Material Inspection Process (P-QD-11)	Project QC Engineer	
Equipment Maintenance & Calibration			
14	Production Manager shall prepare calibration log and Preventive Maintenance Plan and update them accordingly. The plan shall include the following, but not limited to: - Equipment tag number - Required maintenance date	Production Manager	Measuring Equipment Calibration Log. F-P-QD-03-01 Preventive Maintenance Plan F-P-OP-11-02
Reports			
15	Production Manager shall prepare Quarterly report and send it to direct manager for review. Production manager to prepare monthly cost reports indication all related cost breakdown including wastage.	Production Manager	Quarterly Report F-P-OP-11-03

6.3 PROCESS OUTPUT

- Signed Comparison sheet
- Production Plan
- Job Order
- Preventive Maintenance Plan
- Test Results
- External MIR
- Release for Fabrication
- Shipping Release

7. PROCESS RISK ASSESMENT

Included in the Risk register form no. F-P-QD-05-01 "Risk Identification and assessment" maintained by HoD to address risks and opportunities"

8. PROCESS CONTROL

- Actual purchasing and delivery date of materials versus planned/request date.
- Analysis of rejected material.
- Percentage of cost saving from approved budget if applicable.

9. PERFORMANCE MEASURES

- Percentage of cost saving from approved budget if applicable.
- Product Inspection

10. DOCUMENT CHANGE HISTORY

No.	Revision Level	Description of Changes	Effective Date
1	00	New Issue	May, 2025
