


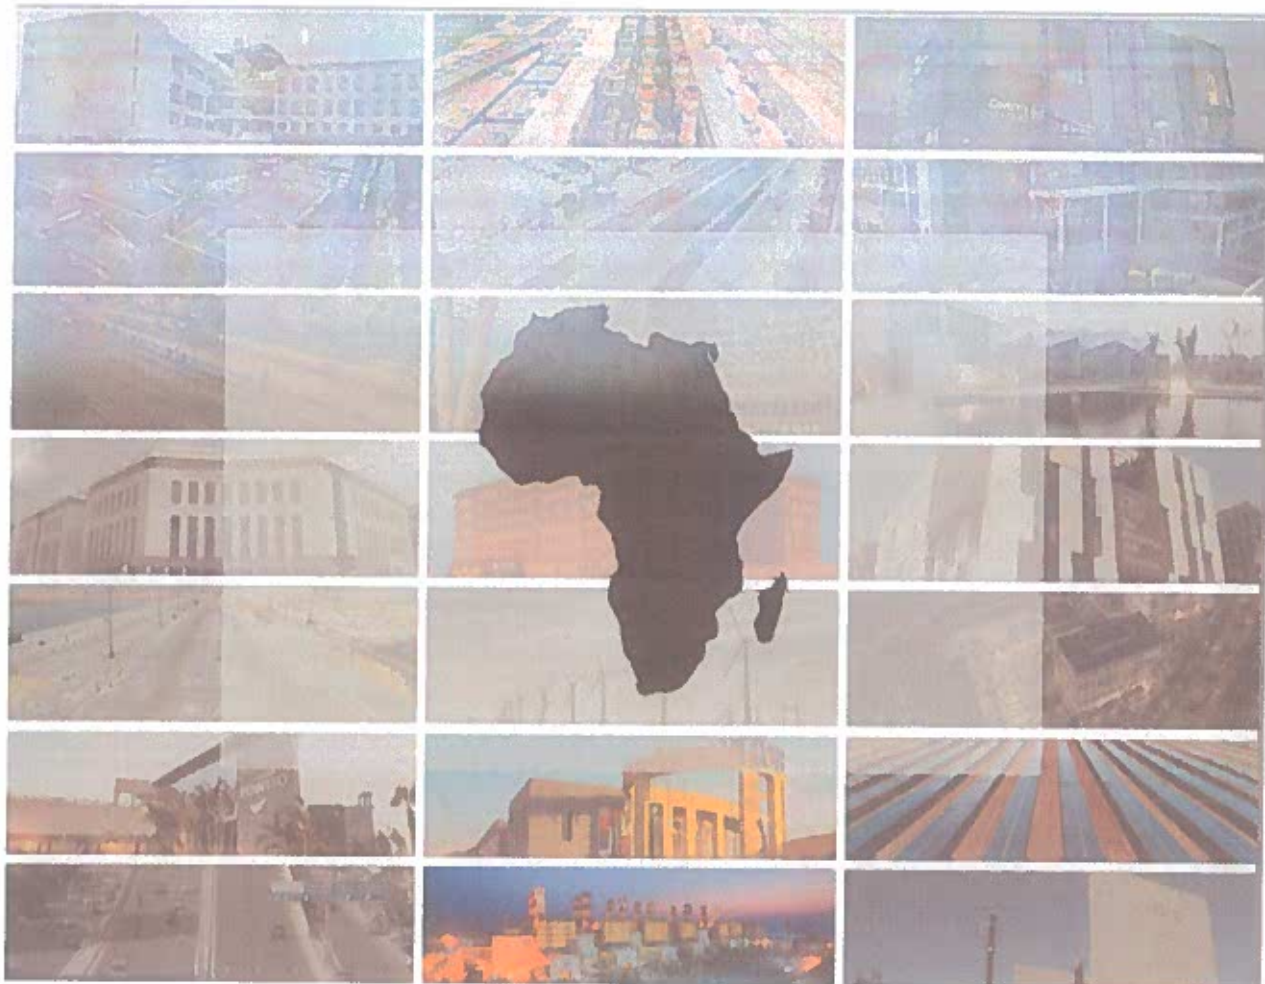

ROWAD
MODERN ENGINEERING

**Control of Records, Filing, Archiving & Backup
Process**
P-QD-08

Prepared by:

Maha Iskander
Quality Assurance Manager

Reviewed by:

Mohamed Ragab
COO

Approved by:

Mohamed Mahlab
CEO

March, 2025

	Control of Records, Filing, Archiving and Backup Process		
	Effective Date: March 2025	Rev.: 02	Doc. no.: P-QD-08

1. OBJECTIVES

The objective of this process is to ensure the records are identified, indexed, scanned & stored in appropriate conditions after project completion.

2. STAKEHOLDER

- PM
- DC
- Contracts Department
- Quality Assurance Department
- Warehouse Department
- HSE Department
- IT Department
- CSR Department

3. LIABLE STAKEHOLDER

- PM
- DC
- Quality Assurance Department
- Contracts Department
- IT Department

4. TERMS AND DEFINITION

- **PM:** Project Manager
- **DC:** Document Controller
- **QA:** Quality Assurance
- **PR:** Purchase Request
- **IT:** Information Technology
- **HSE:** Health, Safety & Environment
- **ERP:** Enterprise Resource Planning (Oracle)
- **Record:** This is a type of document providing evidence that activities have been performed, and results have been achieved. Records can be used to show that traceability requirements are being met, verification is being performed, and preventive and corrective actions are being carried out.

5. RELATED DOCUMENTED INFORMATION

- Box Draft form, F-P-QD-08-01
- Documents Sheet Log, F-P-QD-08-02
- E-filling Index, F-P-QD-08-03
- Project e-Filling Matrix, F-P-QD-08-04
- Documents Storage Log, F-P-QD-08-05
- Documents Handover Checklist, F-P-QD-08-06
- Fit Out Project e-Filling Matrix, F-P-QD-08-07
- Distribution Matrix, F-P-QD-08-08
- Document Submission Guideline, F-P-QD-08-09
- Documents Retention Guideline, F-P-QD-08-10
- Document Control Audit Report, F-P-QD-01-07
- DCs Audit Checklist, F-P-QD-01-08
- Internal Memo, F-P-QD-06-03

6. PROCESS DETAILS

6.1. PROCESS INPUT

- All Project's Documents 
- E-filling Matrix

6.2. PROCESS OPERATION

Sr.	Process Cycle Description	Responsibility	Form
Project Award			
1	Once a project is awarded, QA shall create the project's e-filling on SharePoint. QA shall provide access as per the provided project's staff list.	QA	Project e-Filling Matrix F-P-QD-08-04
2	All project teams shall follow the e-filling matrix to save all project records (soft copies) adhering to the provided access on Rowad server.		Project e-Filling Matrix F-P-QD-08-04
Preparation			
3	Once the project starts, PM shall prepare and approve the distribution matrix to be followed by the DC throughout the project.	PM	Distribution Matrix F-P-QD-08-08

Control of Records, Filing, Archiving and Backup Process

Effective Date: March 2025

Rev.: 02

Doc. no.: P-QD-08

Sr.	Process Cycle Description	Responsibility	Form
4	If the client does not provide a specific coding system, our standard coding system shall be applied to all external forms. DC shall follow the guidelines for document submission, including naming, unique reference numbers or codes for each document for easy tracking & creating logs.		Document Submission Guideline F-P-QD-08-09
5	DC shall ensure that all documents follow approved company templates.	DC	
Maintaining Documents			
6	DC shall maintain the project files and ensure that they are organized and labeled.	DC	File Label
7	DC shall keep track of revisions and ensure logs are up to date and latest revisions are in use.	DC	
8	DC shall distribute documents to designated recipients or stakeholders based on the approved distribution matrix.	DC	
9	DC shall regularly upload digital files to SharePoint for secure archiving.	DC	
10	Backups are securely maintained by IT on daily basis.	IT	
11	QA will conduct regular audits to ensure documents are properly maintained and securely archived. Refer to Internal Audit Process "P-QD-01."	QA	Document Control Audit Checklist F-P-QD-01-08 Document Control Audit Report F-P-QD-01-07
Project Retention at Closeout			
12	At the project completion, PM shall request from QA via email to archive the hardcopies in the company store as per the contract's retention period.	PM	

Sr.	Process Cycle Description	Responsibility	Form
13	Project DC shall issue PR for the required carton boxes to archive the project's record files. Project DC shall prepare the boxes and 2 copies of the Box Draft form for each box, one inside box, and the other to be stuck on the box from outside, following the guideline of Documents Retention at Close-out.	DC	Box Draft Form F-P-QD-08-01 Documents Retention at Close-out F-P-QD-08-10
14	Upon completion of preparing the boxes, DC shall send the Documents Sheet Log signed by DC & PM via an email to the QA.	DC PM	Documents Sheets Log F-P-QD-08-02
14	QA shall conduct a random inspection within 2 days from receiving the Documents Sheet Log, through a site visit to ensure proper storage, labeling, and identification.	QA	Box Draft Form F-P-QD-08-01 Documents Sheet Log F-P-QD-08-02 Documents Handover Checklist F-P-QD-08-06 Documents Retention at Close-out F-P-QD-08-10
15	PM in cooperation with QA shall arrange to transfer the boxes to the warehouse/company's defined storage area. QA shall receive the boxes and sign the Document Sheet Log.	PM QA	Documents Sheets Log F-P-QD-08-02
16	QA shall update the Documents Storage Log and follow up on the retention time to dispose files accordingly.	QA	Documents Storage Log F-P-QD-08-05
Project Documents Disposal			
17	Once the contractual, legal, and company-defined retention period has passed records may be destroyed.		
18	Internal Memo to be issued by QA, and approval of the Contracts Manager & COO must be gained before documents disposal. CC: CSR, HSE, and Warehouse.	QA	Internal Memo F-P-QD-06-03

	Control of Records, Filing, Archiving and Backup Process		
	Effective Date: March 2025	Rev.: 02	Doc. no.: P-QD-08

6.3. PROCESS OUTPUT

- Documents Storage Log clarifying records retention period.
- Project's Records.

7. PROCESS RISK ASSESSMENT

- Included in the Risk register form no. F-P-QD-05-01 "Risk Identification and assessment" maintained by HoD to address risks and opportunities"

8. PROCESS CONTROL

- Documents archiving, awareness & inspection.
- Document Control Audit.
- Update the Storage Log.

9. PERFORMANCE MEASURE

- Track & access project file records easily after project completion.

10. DOCUMENT CHANGE HISTORY

No.	Revision Level	Description of changes	Effective Date
0	00	Major Changes due to transition from ISO 9001:2008 to 9001:2015	01/12/2016
1	01	All	31/01/2022
2	02	1, 3-12 & 18	23/03/2025
