


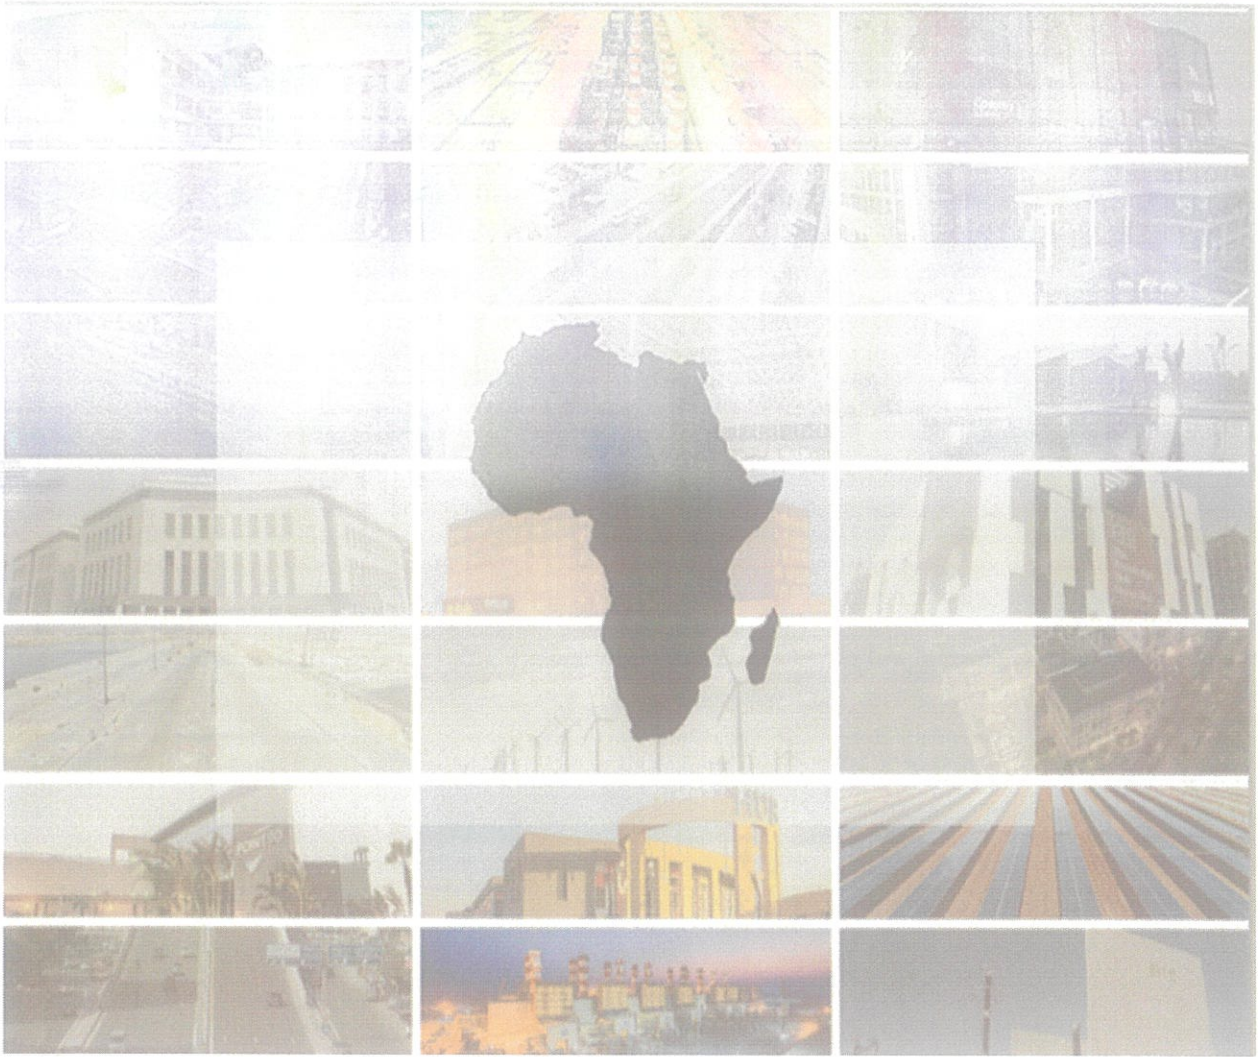

**ROWAD**  
MODERN ENGINEERING

**Procurement Process**  
**P-VMO-02**

**Prepared by:**

Ahmed Helmy

Procurement Manager

*Ahmed*  
*12.26*

Rabie El-Akkad

MEP Manager

*Rabie*  
*2/2/2026*

**Reviewed by:**

Mohamed Ragab

COO

*[Signature]*

**Approved by:**

Mohamed Mahlab

CEO

**January 2026**

*[Signature]*

|                                                                                   |                               |             |                    |
|-----------------------------------------------------------------------------------|-------------------------------|-------------|--------------------|
|  | Procurement Process           |             |                    |
|                                                                                   | Effective Date: January, 2026 | Rev. No.:02 | Doc. No.: P-VMO-02 |

## 1. OBJECTIVES

The procurement (Civil, Arch, MEP) process objective is to ensure the timely and cost-effective acquisition of all types of contracts, reinforce alignment between Procurement and Operations, uphold contractual and technical compliance, and enable successful project execution through transparent and efficient procurement practices.

## 2. STAKEHOLDER

- VMO
- Site team
- PM
- BUM
- Projects Control
- Site T.O
- COO
- H.O Procurement (Civil, Arch, MEP)
- Finance

## 3. TERMS AND DEFINITION

- **H.O.:** Head Office
- **BUM:** Business Unit Manager
- **PM:** Project Manager
- **T.O:** Technical Office
- **TOM:** Technical Office Manager
- **CS:** Comparison Sheet
- **RFQ:** Request for Quotation
- **BOQ:** Bill of Quantity
- **Vendor:** Subcontractors/supplier/service provider
- **LPO:** LPO Contract is a binding agreement with a supplier based on the terms of a Local Purchase Order for goods or services
- **IPO:** IPO Contract is a binding agreement with a supplier based on the terms of an international Purchase Order for goods or services
- **VMO:** Vendor Management Office (Procurement/Purchasing/MEP)
- **Committee Members:** Technical Office, VMO HoD, Finance & COO or their representatives/deputies.

|                                                                                   |                               |             |                    |
|-----------------------------------------------------------------------------------|-------------------------------|-------------|--------------------|
|  | Procurement Process           |             |                    |
|                                                                                   | Effective Date: January, 2026 | Rev. No.:02 | Doc. No.: P-VMO-02 |

#### 4. RELATED DOCUMENTED INFORMATION

- Technical Compliance Sheet, F-P-VMO-02-03
- Contracts Log, F-P-VMO-02-06
- Postponed Payment Request, F-P-VMO-02-07
- Lessons Learned, F-P-VMO-02-08
- Request for Quotation (RFQ), F-P-VMO-01-01
- Supply Engineering Material - Comparison Sheet (CS), F-P-VMO-01-02
- Procurement Approval Authority Matrix, F-P-VMO-01-07
- Supply-Apply Comparison Sheet, F-P-VMO-01-08
- Supply Apply Subcontract Template (Less than 2M), F-P-CN-01-14
- Supply Apply Subcontract Template (2M-5M), F-P-CN-01-15
- Supply Apply Subcontract Template (More than 5M), F-P-CN-01-16
- S/C Deviation Report, F-P-CN-01-20
- Transmittal Log, F-P-PU-01-02
- Payment Plan, F-P-PU-01-06
- Material Submittal, F-PQP-01-02
- Project Strategy (Scope of Work); F-P-TN-02-05
- Procurement (Sourcing) Plan; F-P-TN-02-07
- LPO
- IPO

#### 5. PROCESS DETAILS

##### 6.1 PROCES INPUT

- Tender Documents
- BOQ
- Approved and evaluated vendors

|                                                                                   |                                      |                     |                           |
|-----------------------------------------------------------------------------------|--------------------------------------|---------------------|---------------------------|
|  | <b>Procurement Process</b>           |                     |                           |
|                                                                                   | <b>Effective Date:</b> January, 2026 | <b>Rev. No.:</b> 02 | <b>Doc. No.:</b> P-VMO-02 |

## 5.2 PROCESS OPERATIONS

| Sr. | Process Cycle Description                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | Responsibility                              | Forms                                                       |
|-----|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------|-------------------------------------------------------------|
| 1   | <p>H.O Procurement (MEP, Civil, Arch) shall issue Project Strategy (Scope of Work) within 7 working days from Tender Handover Meeting and uploading documents on server after discussing the items with Tendering, PM/BUM, and Projects Control according to the project schedule, BOQ, specs and budget, and define any added or omitted items.</p> <p>Project Strategy (Scope of Work) shall be approved by PM/BUM within 1 day, then to be sent to Projects Control to consider it in the baseline &amp; procurement (sourcing) plan preparation.</p> | <p>H.O Procurement</p> <p>BUM</p> <p>PM</p> | <p>Project Strategy (Scope of Work)</p> <p>F-P-TN-02-05</p> |
| 2   | <p>Material list along with the duration to be uploaded on Unifier by HO Procurement within 7 working days from Tender handover meeting</p> <p>Approved project Strategy (Scope of Work) to be uploaded on unifier by VMO.</p>                                                                                                                                                                                                                                                                                                                           | <p>PM/BUM</p> <p>Projects Control</p>       | <p>Project Strategy (Scope of Work)</p> <p>F-P-TN-02-05</p> |
| 3   | <p>Procurement, Projects Control and BUM to be informed in case PM updates Project Strategy (Scope of Work) throughout the project, or vice versa, on monthly basis if required. Procurement plan to be updated via Unifer by VMO accordingly including the updated way of acquisition.</p>                                                                                                                                                                                                                                                              | <p>PM</p> <p>VMO</p>                        | <p>Project Strategy (Scope of Work)</p> <p>F-P-TN-02-05</p> |

|                                                                                   |                                      |                     |                           |
|-----------------------------------------------------------------------------------|--------------------------------------|---------------------|---------------------------|
|  | <b>Procurement Process</b>           |                     |                           |
|                                                                                   | <b>Effective Date:</b> January, 2026 | <b>Rev. No.:</b> 02 | <b>Doc. No.:</b> P-VMO-02 |

| <b>Sr.</b> | <b>Process Cycle Description</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | <b>Responsibility</b>                     | <b>Forms</b>                                                                                                                                                |
|------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 4          | <p>H.O Procurement shall create RFQ material reference record on unifier prior start the RFQ Cycle.</p> <p>Procurement shall prepare work packages for RFQ submission including the below to the approved vendors, then review the received technical compliance sheet for all received quotations and upload it on Unifier:</p> <ol style="list-style-type: none"> <li>1. Draft contract (Mandatory) (received the BTB template from contract department)</li> <li>2. Draft Bonds/LG's (if applicable)</li> <li>3. Project Stamped Specification</li> <li>4. Project Latest Stamped Drawings</li> <li>5. Blank BOQ with items to price</li> <li>6. Technical Compliance Sheet</li> <li>7. Schedule (received from Project Control Department)</li> <li>8. Others (Tender clarifications, etc.)</li> </ol> <p>Procurement Engineer shall frequently update the RFQ during bidding phase in case of any changes and upload the relevant offers (attachments) on Unifier.</p> <p>Refer to Procurement Approval Authority Matrix "F-P-VMO-01-07"</p> | <p>H.O<br/>Procurement</p> <p>TO</p>      | <p>RFQ<br/>F-P-VMO-01-01</p> <p>Technical<br/>Compliance Sheet<br/>F-P-VMO-02-03</p> <p>Procurement<br/>Approval Authority<br/>Matrix<br/>F-P-VMO-01-07</p> |
| 5          | <p>H.O. Procurement shall prepare material submittals and send them to site TO to submit it to consultant &amp; client to obtain the final approval.</p> <p>Transmittal Log to be updated by HO Procurement accordingly</p>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | <p>H.O<br/>Procurement</p> <p>Site TO</p> | <p>Material Submittal<br/>F-PQP-01-02</p> <p>Transmittal Log<br/>F-P-PU-01-02</p>                                                                           |
| 6          | <p>Site TO Manger shall confirm on Unifier if technical compliance requires his approval as per the project Procurement plan.</p> <p>If TO approval is required, Site TO shall review the technical compliance, then approve/ Reject with comments</p> <p>In case of rejection, H.O procurement shall resubmit to obtain TO approval prior CS final approval.</p>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 | <p>Site TO</p> <p>H.O<br/>Procurement</p> | <p>Technical<br/>Compliance Sheet<br/>F-P-VMO-02-03</p>                                                                                                     |

|                                                                                   |                                      |                     |                           |
|-----------------------------------------------------------------------------------|--------------------------------------|---------------------|---------------------------|
|  | <b>Procurement Process</b>           |                     |                           |
|                                                                                   | <b>Effective Date:</b> January, 2026 | <b>Rev. No.:</b> 02 | <b>Doc. No.:</b> P-VMO-02 |

| <b>Sr.</b> | <b>Process Cycle Description</b>                                                                                                                                                                                                                                                                                                                                                                                                                   | <b>Responsibility</b> | <b>Forms</b>                                                                                                                                                                        |
|------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 7          | <p>The Procurement Team shall prepare a Commercial comparison for all received quotations versus the budget, with a minimum of three vendors,</p> <p>CS approval after finalizing the technical compliance sheet along with time frame, refer to (Procurement Approval Authority Matrix F-P-VMO-01-07)</p> <p>If fewer than three quotations are collected, the reason for not meeting the minimum requirement shall be identified in Unifier.</p> | H.O<br>Procurement    | <p>Supply Engineering Material - Comparison Sheet, F-P-VMO-01-02</p> <p>Supply-Apply Comparison Sheet, F-P-VMO-01-08</p> <p>Procurement Approval Authority Matrix F-P-VMO-01-07</p> |
| 8          | <p>For critical cases, Commercial offers are restricted and can only be accessed by the committee on a specific date defined by the COO. Whereas the critical cases will be defined in the project execution plan and during the Operation coordination meeting.</p> <p>Committee Members or their representatives/deputies to discuss the commercial closed offer for final decision.</p>                                                         | Committee Members     |                                                                                                                                                                                     |
| 9          | <p>S/C Deviation report to be attached with all comparison sheets all limits along with Apply contracts, S&amp;A contracts and LPOs/IPOs.</p> <p>COO and Contracts signature is required as per the approved matrix.</p>                                                                                                                                                                                                                           | H.O<br>Procurement    | S/C Deviation report F-P-CN-01-20                                                                                                                                                   |
| 10         | <p>"Lessons Learned" form shall be used during comparison sheet preparation for tolerance 10% more (profit) or less (loss) and then to be uploaded on unifier and CC Tendering department for information and future consideration.</p>                                                                                                                                                                                                            | H.O<br>Procurement    | Lessons Learned F-P-VMO-02-08                                                                                                                                                       |
| 11         | <p>After final vendor selection, H.O. Procurement shall issue subcontract agreement/LPO/IPO according to templates issued by Contracts.</p> <p>Refer to Subcontract Agreement Process (P-CN-01)</p>                                                                                                                                                                                                                                                | H.O<br>Procurement    | <p>Subcontract Agreement Templates F-P-CN-01-14/15/16</p>                                                                                                                           |

|                                                                                   |                               |             |                    |
|-----------------------------------------------------------------------------------|-------------------------------|-------------|--------------------|
|  | Procurement Process           |             |                    |
|                                                                                   | Effective Date: January, 2026 | Rev. No.:02 | Doc. No.: P-VMO-02 |

| Sr. | Process Cycle Description                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                   | Responsibility                                                    | Forms                                         |
|-----|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------|-----------------------------------------------|
| 12  | H.O. Procurement shall send the agreement (Subcontract/LPO/IPO) to the selected vendors and negotiate the terms & conditions till final approved copy, and then follow-up till the final subcontract/LPO/IPO is signed<br><br>Refer to SC Agreement Signature Matrix "F-P-CN-01-11"                                                                                                                                                                                                                                                                                                         | H.O<br>Procurement                                                |                                               |
| 13  | HO Procurement shall ensure that Procurement plan is updated with actual dates.<br><i>(Unifier: Created RFQ Material Records to be linked with procurement plan lines).</i>                                                                                                                                                                                                                                                                                                                                                                                                                 | H.O<br>Procurement                                                |                                               |
| 14  | H.O Procurement shall update contracts log on bi-weekly basis.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | H.O<br>Procurement                                                | Contracts Log<br>F-P-VMO-02-06                |
| 15  | H.O Procurement (Civil, Arch, MEP) shall send the relevant Payment Plan to PM on monthly basis.<br>The PM shall prepare the Monthly Payment Plan for the whole project, covering all payment types (Petty cash, Advance Payments, Due payments and Payments against delivery), then Payment plan shall be approved by BUM.<br><br>Priorities shall be determined by the BUM, after discussion with the COO, and based on the available funds.<br><br>The finalized Payment Plan shall be submitted to Finance via email, with all priorities clearly identified, to enable payment release. | H.O<br>Procurement<br><br>PM<br><br>BUM<br><br>COO<br><br>Finance | Payment Plan<br>F-P-PU-01-05                  |
| 16  | H.O. Procurement/PM in coordination with BUM shall issue Postponed Payment Request according to the project's need, then send it to Finance to clarify the overall Postponed status, followed by CFO & COO approval.                                                                                                                                                                                                                                                                                                                                                                        | H.O<br>Procurement/PM<br><br>BUM<br><br>CFO<br><br>COO            | Postponed Payment<br>Request<br>F-P-VMO-02-07 |

