


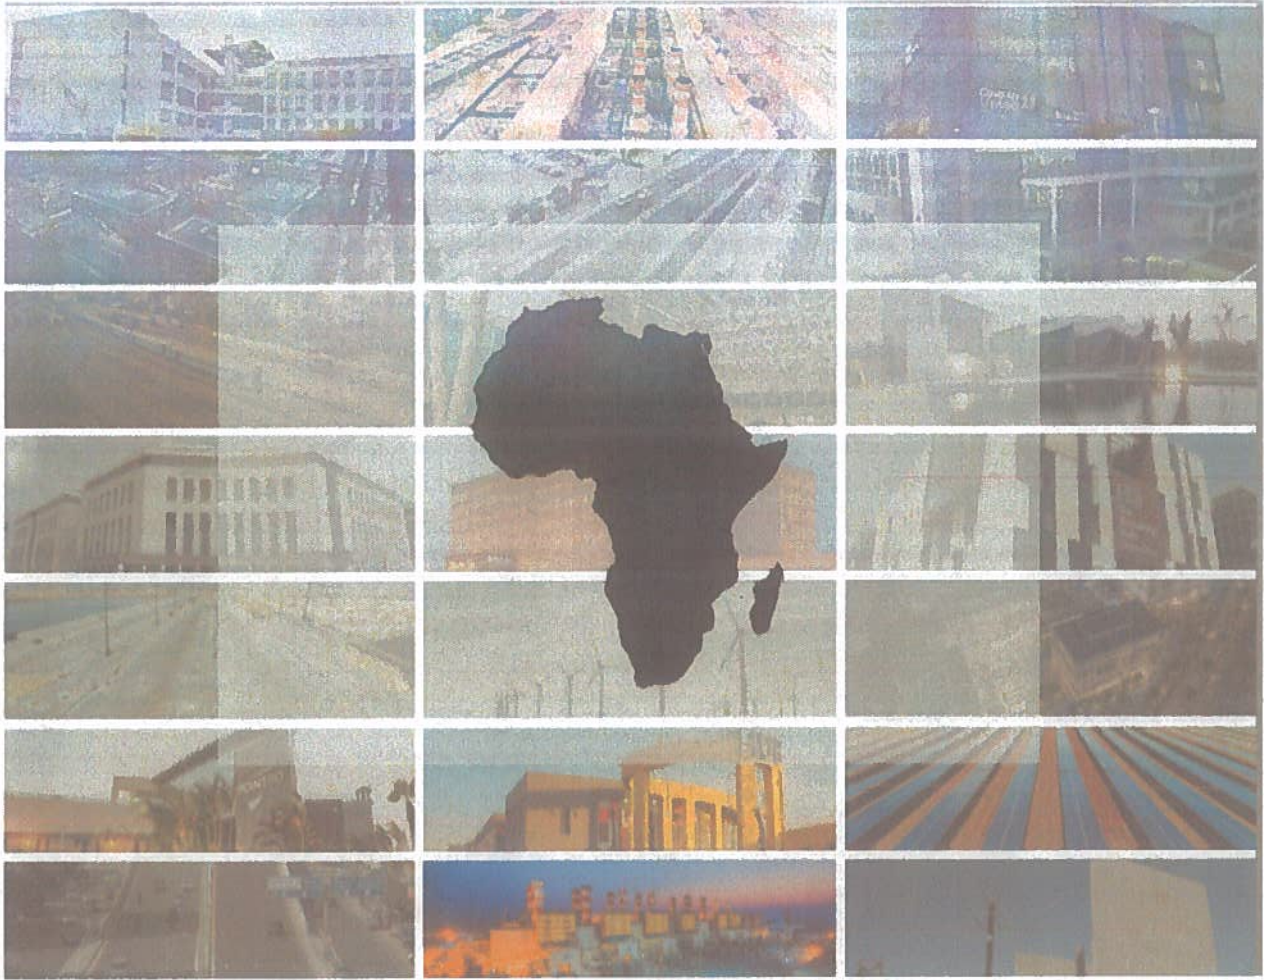

Project Initiation Process P-TN-01

Prepared by:

Mohamed Sultan
Tendering Manager

Reviewed by:

Mostafa El-Saadany
Technical Director

Mohamed Ragab
COO

Approved by:

Mohamed Mahlab
CEO

July, 2025

Ahmed Gamal
Contracts Manager

Yasser El-Saadany
Commercial Director

1. OBJECTIVES

The objective of this process is to discuss and review the organization's ability to meet the requirements of a new project and to identify the steps to be taken to reach a decision on accepting the business opportunity, followed by the estimation process till tender submission in details or apology to the client.

2. STAKEHOLDER

- Tendering
- Commercial
- Contracts
- Operations
- HSE
- Finance
- COO
- CEO

3. TERMS AND DEFINITIONS

- **RFP:** Request for Proposal
- **RFQ:** Request for quotation
- **MoM:** Minutes of Meetings
- **CS:** Comparison Sheet
- **HoD:** Head of Department
- **CEO:** Chief Executive Office
- **COO:** Chief Operation Officer
- **Brown Field:** New projects which have an old phase/extension.
- **Green Field:** New projects with no old phases/extension.

4. RELATED DOCUMENTED INFORMATION

- Tender RFQ, F-P-TN-01-01
- Site Visit Form, F-P-TN-01-02
- Tender Top sheet Template, F-P-TN-01-03
- Tender Study Log, F-P-TN-01-04
- Go or No Go, F-P-TN-01-06
- Contract Qualifications, F-P-TN-01-08
- Tender CS, F-P-TN-01-10
- Project Initiation Flowchart, F-P-TN-01-12
- Risk Assessment, F-P-QD-05-01
- Minutes of Meeting, F-P-QD-06-02
- Letter Template, F-P-QD-06-04

	Project Initiation Process		
	Effective Date: July, 2025	Rev. No.: 04	Doc. No.: P-TN-01

5. PROCESS DETAILS

5.1. PROCESS INPUT

- Project information
- Documents received from the client.

5.2.PROCESS OPERATION

Sr.	Process Cycle Description	Responsibility	Form
1	<u>GO or No GO</u> After receiving RFQ/ RFP/tender announcement/ invitation from the client, the Commercial shall prepare the Go or No Go form within 24 hrs. from receiving the documents and send it to Tendering, COO and CEO for decision.	Commercial dept.	Go or No Go F-P-TN-01-06
2	If the decision is not to proceed with the project study, the Commercial shall send a letter of apology to the client who sent the RFP/RFQ. If the decision is to study the project, the commercial shall upload Contract documents on Head office server and notify Tendering and Contracts	Commercial dept.	Letter Template F-P-QD-06-04
3	The Tendering Manager shall initiate the estimation process and assign a Tender Coordinator. Subsequently, relevant information will be collected from various departments to facilitate the project study, and a site visit will be conducted if necessary. During the estimation process a site visit shall be arranged to check the actual site conditions (Operation department might join the visit in case it is a brown field & not a green field) and a site visit report shall be prepared by Tendering and sent to the concerned parties.	Tendering Manager	Site visit Report F-P-TN-01-02
4	Commercial shall hold initial Project alignment meeting with Legal, Finance, Tendering and Contracts within 5 days from documents distribution. MOM to be issued to discuss preparation needed for proposal submission.	Commercial dept.	MOM F-P-QD-06-02
5	Commercial shall receive trade risk reports from Finance, HSE, Legal, and send to Tendering & Contracts 7 days after the meeting unless agreed otherwise.	Commercial dept.	
6	Project Presentation to be prepared and sent to COO & CEO 2 days from receiving the risks, including major contractual risks by Contracts.	Tendering Contracts	

	Project Initiation Process		
	Effective Date: July, 2025	Rev. No.: 04	Doc. No.: P-TN-01

Sr.	Process Cycle Description	Responsibility	Form
7	<u>If Tendering and commercial decide not to bid during the study</u> Tendering may initiate a meeting with the Commercial, COO & CEO. Commercial shall notify all stakeholders, including the Contracts Department, via email.	Tendering Commercial	
8	Tendering shall finalize the direct cost upon receiving supplier/subcontractor offers and prepare the comparison sheet accordingly, and send a weekly follow-up log for projects under study to concerned parties.	Tendering	Tender RFQ F-P-TN-01-01 Tender CS F-P-TN-01-10
9	Contracts shall prepare and send contractual Risk Assessment to Tendering 7 days before submission for all projects limits.	Contracts	Risk Assessment F-P-QD-05-01
10	<u>For Projects >=50M USD (int.) and 1 billion (local)</u> A second alignment meeting shall be held within 5 days before submission with Tendering, Contracts, Finance, COO and CEO.	Commercial Director	Tender Top Sheet F-P-TN-01-03 MOM F-P-QD-06-02
11	Tendering manager shall review the direct and indirect cost prior to bid closing meeting	Tendering	
12	<u>For Projects <50M USD(int.) and 1 billion (Local)</u> Tendering shall hold Bid closing Meeting 2 days before submission with Commercial.	Tendering	Tender Top Sheet F-P-TN-01-03
13	Review client's contract and submit contract qualifications to Tendering and Commercial 2 days before submission.	Contracts	Contract Qualifications F-P-TN-01-08
14	Tendering shall consolidate all required documents for the proposal submission and periodically update the Tender Study Log with the latest submitted price.	Tendering	Tender Study Log F-P-TN-01-04
15	The tendering proposal to be submitted to the client. For Projects >=50M USD (int.) and 1 billion (local), the Final Top Sheet to be signed by the COO and CEO.	Commercial	Tender Top Sheet F-P-TN-01-03
16	<u>In case of project award:</u> Commercial to compile contract document and uploaded to E-filling after signature (within suitable duration) the project client contract to be initiated on Unifier.	Commercial	

	Project Initiation Process		
	Effective Date: July, 2025	Rev. No.: 04	Doc. No.: P-TN-01

Sr.	Process Cycle Description	Responsibility	Form
	<u>In case of an unsuccessful tender proposal:</u> The reasons for the loss shall be identified through stakeholder meetings for lessons learned.		
17	Once the Commercial initiate the project client contract on Unifier, the Contracts shall review and verify the contractual information before forwarding it to the Finance.	Contracts	
18	Commercial Director shall prepare annual analysis report for top management review	Commercial Director	
19	Awarding annual analysis report to be prepared, on target achievement ratio vs. total awarded project value.	Tendering	
20	Monthly meeting to be held between Tendering, Commercial, Contracts, and Finance to review the ongoing project status.	Tendering	

5.3. PROCESS OUTPUT

- Apology letter
- Tender top sheet
- Commercial analysis report & Tender analysis Report
- Signed Client Contract

6. PROCESS RISK ASSESSMENT

Included in the Risk register form no. F-P-QD-05-01 "Risk Identification and assessment" maintained by HOD to address risks and opportunities.

7. PROCESS CONTROL

- Signature of Go or No Go form by Commercial Director, Technical Director, COO and CEO.
- Records shall be maintained by the Commercial for 1 year.
- For awarded projects, Tender Top Sheet shall be reviewed and approved by Tendering Manager, COO, and CEO.

8. PERFORMANCE MEASURE

- Number of received RFP from clients and degree of compliance with company strategy.
- Evaluation of the follow-up by Commercial with client in case of apology or submission of offers.
- Loss Analysis Report.
- Awarding Analysis Report.

	Project Initiation Process		
	Effective Date: July, 2025	Rev. No.: 04	Doc. No.: P-TN-01

9. DOCUMENT CHANGE HISTORY

No.	Revision Level	Description of Changes	Effective Date
1	00	Major Changes due to transition from ISO 9001:2008 to 9001:2015	Dec, 2016
2	01	All points	Sept, 2021
3	02	Responsibilities of Tender Manager, Technical Director, BD Manager & Commercial Manager. Points 10/14/23	May, 2022
4	03	Points: 1, 4-6, 10-12, 14, 18, 22	August, 2024
5	04	All Points	July, 2025
